

Lab 2: Agile Backlog Creation & Sprint Simulation

Jira Deliverable — Student Club Event Ticketing & Budget Portal

Name: Aarush Muralidhara

SRN: PES1UG24CS010

Class: 5A

Project key: SCETBP

1. Project Overview

Project: Student Club Event Ticketing & Budget Portal (key: SCETBP)

The backlog is organized into 4 Epics and 12 User Stories, run across 2 sprints (Sprint 1: 4 stories / 14 points; Sprint 2: 8 stories / 37 points). All 12 stories were marked Done by the end of the two sprints.

2. Epics

Epic ID	Epic Name	Description
SCETBP-1	Event Proposal Management	Enables club leads to create, edit, and submit event proposals.
SCETBP-2	Budget Request & Approval	Enables club leads to request event budgets and route them through multi-stage approval.
SCETBP-3	Ticket Generation & Management	Enables generation, management, and validation of event tickets.
SCETBP-4	Event Monitoring & Administration	Enables tracking of proposal status, approvals, ticketing info, and check-in records.

Screenshot — Backlog with Epics and User Stories (final state, all items Done):

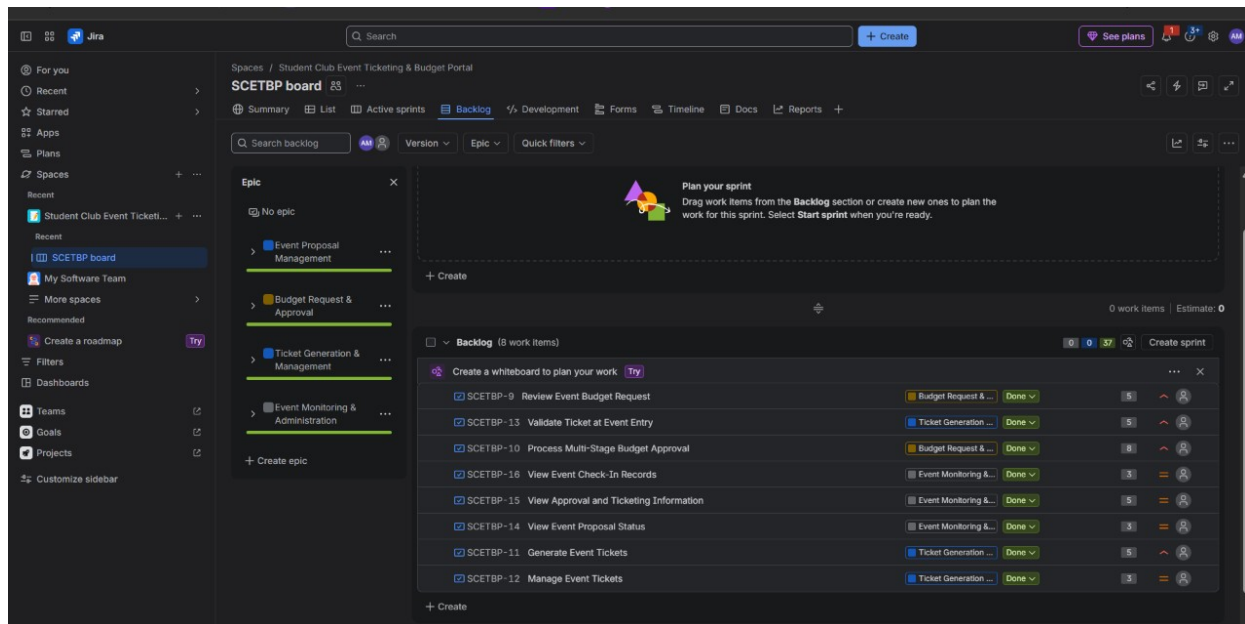


Fig. 1 — Backlog grouped by Epic, all 4 epics at 100% completion

3. User Stories

Sprint 1 stories:

Key	Summary	Epic	Priority	Points
SCETBP-5	As a Club Lead, ... (view/track proposal)	Event Proposal Management	Medium	5
SCETBP-6	Edit Event Proposal	Event Proposal Management	Medium	3
SCETBP-7	As a Club Lead, ... (related proposal action)	Event Proposal Management	Medium	3
SCETBP-8	Submit Event Budget Request	Budget Request & Approval	High	3

Sprint 2 stories:

Key	Summary	Epic	Priority	Points
SCETBP-9	Review Event Budget Request	Budget Request & Approval	High	5
SCETBP-10	Process Multi-Stage Budget Approval	Budget Request & Approval	High	8
SCETBP-11	Generate Event Tickets	Ticket Generation & Management	High	5
SCETBP-12	Manage Event Tickets	Ticket Generation & Management	Medium	3
SCETBP-13	Validate Ticket at Event Entry	Ticket Generation & Management	High	5
SCETBP-14	View Event Proposal Status	Event Monitoring & Administration	Medium	3
SCETBP-15	View Approval and Ticketing Information	Event Monitoring & Administration	Medium	5
SCETBP-16	View Event Check-In Records	Event Monitoring & Administration	Medium	3

Note: SCETBP-5 and SCETBP-7 summaries were truncated to "As a Club Lead, ..." in the source screenshot — replace with their full titles from your Jira project if needed for submission.

4. Story Point Assignments

Sprint 2 backlog with story points assigned (Fibonacci scale) before the sprint was started — total estimate: 37 points across 8 stories.

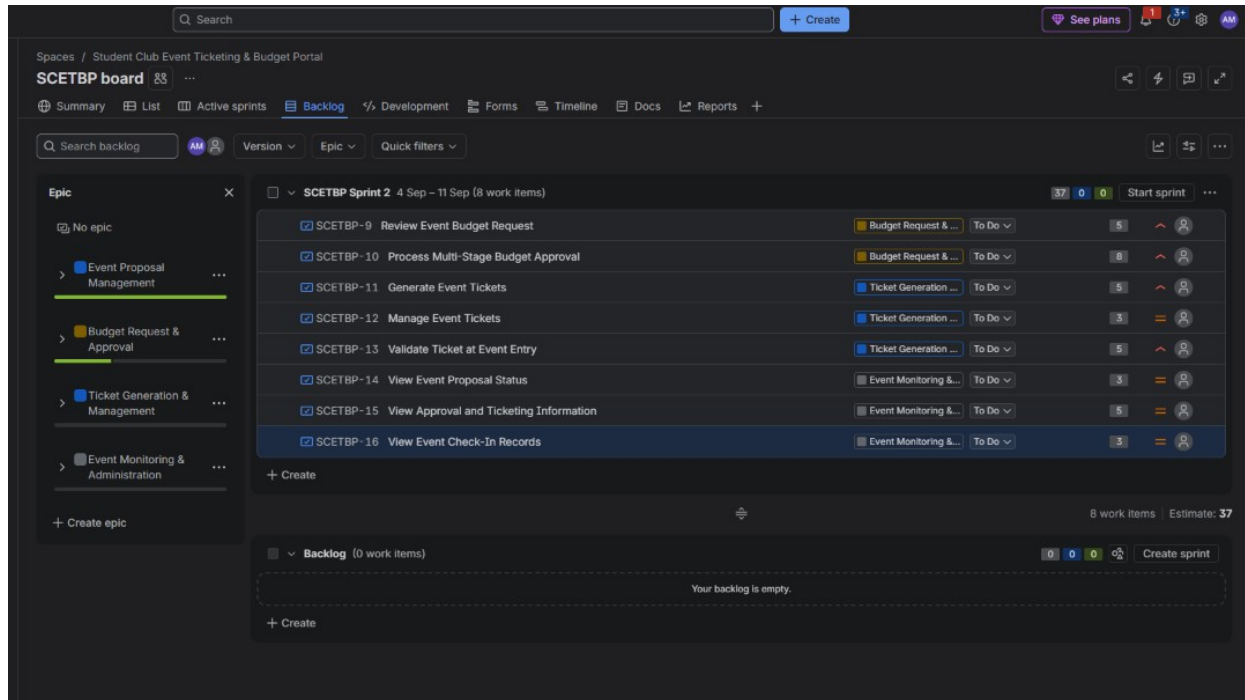


Fig. 2 — Sprint 2 backlog with story points, priority, and status

5. Sprint Board (Active Sprint View)

Sprint 2 in progress: To Do / In Progress / In Review / Done columns.

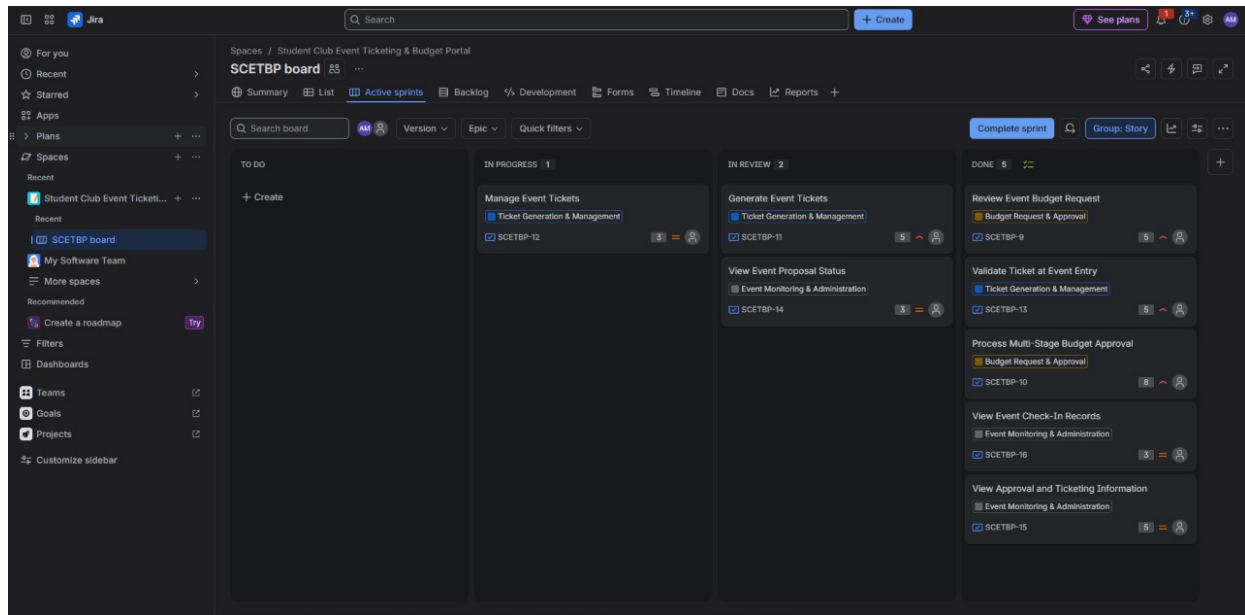


Fig. 3 — Sprint 2 active board mid-sprint (1 In Progress, 2 In Review, 5 Done)

6. Burndown Charts

Sprint 1 (28 Aug – 3 Sep): started at 8 points, grew to 14 as issues were re-estimated after the sprint began.

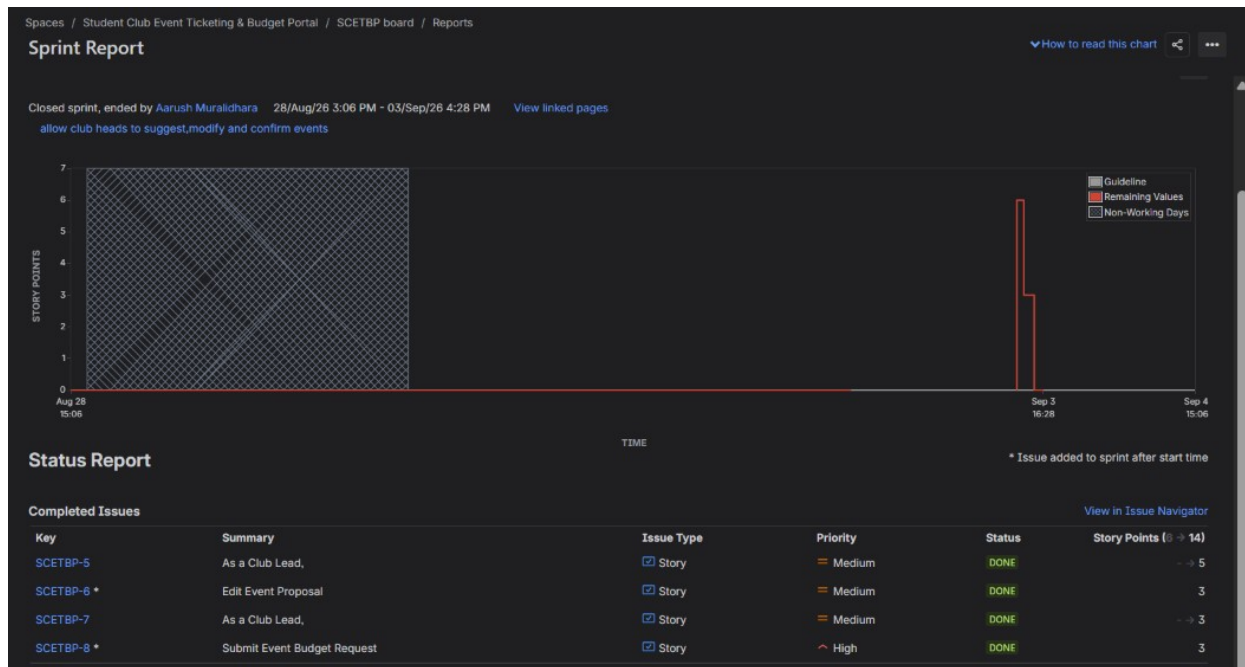


Fig. 4 — Sprint 1 burndown chart (4 stories completed, 14 points)

Sprint 2 (4 Sep – 11 Sep): 8 stories, 37 points, all completed with no scope changes.

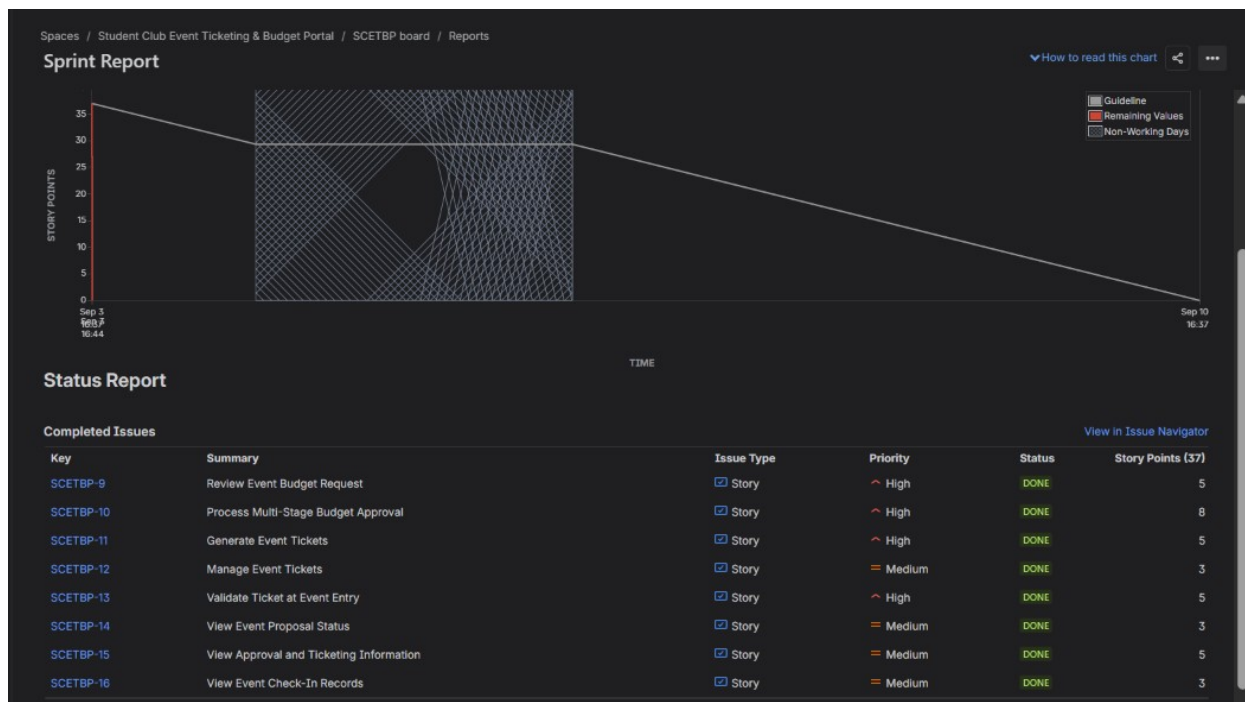


Fig. 5 — Sprint 2 burndown chart (8 stories completed, 37 points)

7. Reflection Questions

Draft answers below are grounded in what the screenshots show. Review and personalize before submitting — add your own team/process observations where the data alone doesn't tell the full story.

1. Did your estimations reflect the actual effort?

Sprint 1's estimate grew from 8 to 14 story points after the sprint had already started (visible in Jira's "Story Points (8 → 14)" scope-change indicator) — meaning some stories were under-estimated at planning time and had to be re-pointed mid-sprint.

Sprint 2, by contrast, was planned and completed at a stable 37 points with no scope changes recorded, suggesting estimation accuracy improved between the two sprints.

2. Was your backlog well-prioritized?

Stories were split between High and Medium priority (no Low/Lowest items used) — e.g. budget-approval and ticket-generation stories were marked High, while most "view/monitoring" stories were Medium.

This is a reasonable priority split, though the absence of any Low-priority items is worth reflecting on — was every remaining story genuinely time-critical, or would finer-grained prioritization have helped sequence the two sprints differently?

3. How did your simulated sprint align with your plan?

Both sprints reached 100% completion — all 4 Sprint 1 stories and all 8 Sprint 2 stories ended in Done, and the Jira "Complete Sprint" confirmation for Sprint 2 explicitly noted "8 completed work items — that's all of them."

No stories were left in To Do or rolled over to a future sprint, indicating the planned scope for each sprint matched what the (simulated) team could deliver.

4. What insights did the burndown chart give about your team's capacity?

Both burndown charts show the same pattern: the red "remaining values" line stays flat near its starting value for most of the sprint window, then drops sharply to zero right at the end (Sprint 1 spikes and drops around Sep 3; Sprint 2 drops almost immediately after the guideline period).

This "flat-then-cliff" shape — rather than a steady decline along the grey guideline — suggests work was logged as Done in a late batch rather than completed incrementally through the sprint, which is common in a simulated/solo sprint. In a real team setting, this pattern would be a signal to break stories down further or check in on progress mid-sprint rather than only at the end.
